

ID	Task Name	Duration	Start	Finish	Predecessors	Jan '12	May '12	Sep '12	Jan '13	May '13	Sep '13	Jan '14	May '14	Sep '14
1	AAMVA E-Titling Scope and Costs (23 Months)	471 d	Mon 7/2/12	Mon 6/9/14										
2														
3	Project Start Date		Mon 7/2/12											
4														
5	Project Management and Reporting	460 d	Mon 7/2/12	Thu 5/22/14	3									
6	Weekly Meetings and Monthly Status Reports	460 d	Mon 7/2/12	Thu 5/22/14										
7	Project Planning	24 d	Mon 7/2/12	Fri 8/3/12	3									
8	Develop Project Plan	24 d	Mon 7/2/12	Fri 8/3/12										
9	Draft 1 Development	8 d	Mon 7/2/12	Thu 7/12/12										
10	Draft 1 Task Force Review	5 d	Fri 7/13/12	Thu 7/19/12	9									
11	Draft 1 Task Force Teleconference	1 d	Fri 7/20/12	Fri 7/20/12	10									
12	Draft 2 Revisions	5 d	Mon 7/23/12	Fri 7/27/12	11									
13	Draft 2 Task Force Review	4 d	Mon 7/30/12	Thu 8/2/12	12									
14	Draft 2 Task Force Teleconference Review and Approval	1 d	Fri 8/3/12	Fri 8/3/12	13									
15	Project Plan Approved	0 d	Fri 8/3/12	Fri 8/3/12	14									
16	Assemble Task Force and Teams	24 d	Mon 7/2/12	Fri 8/3/12										
17	Task Force and Teams (Business, Legal, Technical)	24 d	Mon 7/2/12	Fri 8/3/12										
18														
19	Prepare Infrastructure and Data Integration Standards	139 d	Mon 8/6/12	Tue 3/12/13	7									
20	Task Force Meeting #1	22 d	Mon 8/6/12	Wed 9/5/12										
21	Prepare for Meeting #1	20 d	Mon 8/6/12	Fri 8/31/12										
22	Conduct Meeting #1 (travel covered by FY12 E-Title committee budget)	2 d	Tue 9/4/12	Wed 9/5/12	21									
23	Follow Ups for Meeting #1	5 d	Mon 8/6/12	Fri 8/10/12										
24	Business Team	38 d	Thu 9/6/12	Tue 11/6/12	20									
25	Roadmap for E-Titling	38 d	Thu 9/6/12	Tue 11/6/12										
26	Draft 1 Development	20 d	Thu 9/6/12	Wed 10/3/12										
27	Draft 1 Review	5 d	Thu 10/4/12	Thu 10/18/12	26									
28	Draft 1 Teleconference	1 d	Fri 10/19/12	Fri 10/19/12	27									
29	Draft 2 Revisions	7 d	Mon 10/22/12	Tue 10/30/12	28									
30	Draft 2 Review	4 d	Wed 10/31/12	Mon 11/5/12	29									
31	Draft 2 Teleconference Review and Approval	1 d	Tue 11/6/12	Tue 11/6/12	30									
32	Roadmap Approved	0 d	Tue 11/6/12	Tue 11/6/12	31									
33	Technical Team	117 d	Thu 9/6/12	Tue 3/12/13	20									
34	Develop Standardized Data Definition for E-Titling Record	79.88 d	Thu 9/6/12	Thu 1/17/13										
35	Draft 1 Development	46.88 d	Thu 9/6/12	Mon 11/19/12										
36	Draft 1 Task Force Review	10 d	Mon 11/19/12	Wed 12/5/12	35									
37	Draft 1 Task Force Teleconference Review	1 d	Wed 12/5/12	Thu 12/6/12	36									
38	Draft 2 Revisions	16 d	Thu 12/6/12	Tue 1/8/13	37									
39	Draft 2 Task Force Review	5 d	Tue 1/8/13	Wed 1/16/13	38									
40	Draft 2 Task Force Teleconference Review and Approval	1 d	Wed 1/16/13	Thu 1/17/13	39									
41	Standardized Data Definition Approved	0 d	Thu 1/17/13	Thu 1/17/13	40									
42	Develop MCO Verification Service	117 d	Thu 9/6/12	Tue 3/12/13										
43	Requirements	40 d	Thu 9/6/12	Thu 11/8/12										
44	Draft 1 Development	15 d	Thu 9/6/12	Wed 9/26/12										
45	Draft 1 Task Force Review	10 d	Thu 9/27/12	Thu 10/18/12	44									
46	Draft 1 Task Force Teleconference Review	1 d	Fri 10/19/12	Fri 10/19/12	45									
47	Draft 2 Revisions	8 d	Mon 10/22/12	Wed 10/31/12	46									
48	Draft 2 Task Force Review	5 d	Thu 11/1/12	Wed 11/7/12	47									
49	Draft 2 Task Force Teleconference Review and Approval	1 d	Thu 11/8/12	Thu 11/8/12	48									
50	Requirements Approved	0 d	Thu 11/8/12	Thu 11/8/12	49									
51	Jurisdiction SDD	44 d	Fri 11/9/12	Wed 1/23/13	43									
52	Draft 1 Development	20 d	Fri 11/9/12	Mon 12/10/12										
53	Draft 1 Task Force Review	10 d	Tue 12/11/12	Wed 1/2/13	52									
54	Draft 1 Task Force Teleconference Review	1 d	Thu 1/3/13	Thu 1/3/13	53									
55	Draft 2 Revisions	7 d	Fri 1/4/13	Tue 1/15/13	54									
56	Draft 2 Task Force Review	5 d	Wed 1/16/13	Tue 1/22/13	55									
57	Draft 2 Task Force Teleconference Review and Approval	1 d	Wed 1/23/13	Wed 1/23/13	56									


Project: E-Titling Proof of Concept
Date: Wed 4/4/12

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Progress	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Jan '12	May '12	Sep '12	Jan '13	May '13	Sep '13	Jan '14	May '14	Sep '14
58	Jurisdiction SDD Approved	0 d	Wed 1/23/13	Wed 1/23/13	57				1/23					
59	System Design	12 d	Thu 1/24/13	Fri 2/8/13	51									
60	Development	7 d	Thu 1/24/13	Fri 2/1/13										
61	Review/Finalize SDD	5 d	Mon 2/4/13	Fri 2/8/13	60									
62	Development	13 d	Mon 2/11/13	Thu 2/28/13	59									
63	Set up environments, UNI updates and system testing	13 d	Mon 2/11/13	Thu 2/28/13										
64	QA/Test	19 d	Mon 2/11/13	Fri 3/8/13	59									
65	Acceptance testing	12 d	Mon 2/11/13	Wed 2/27/13										
66	Structured test planning	7 d	Thu 2/28/13	Fri 3/8/13	65									
67	Deployment	2 d	Mon 3/11/13	Tue 3/12/13	64,62									
68	Prepare UNI software release	2 d	Mon 3/11/13	Tue 3/12/13										
69	MCO Verification Service Complete	0 d	Tue 3/12/13	Tue 3/12/13	67				3/12					
70	AAMVA ELT Service	40 d	Thu 9/6/12	Thu 11/8/12										
71	Requirements	40 d	Thu 9/6/12	Thu 11/8/12										
72	Draft 1 Development	15 d	Thu 9/6/12	Wed 9/26/12										
73	Draft 1 Task Force Review	10 d	Thu 9/27/12	Thu 10/18/12	72									
74	Draft 1 Task Force Teleconference Review	1 d	Fri 10/19/12	Fri 10/19/12	73									
75	Draft 2 Revisions	8 d	Mon 10/22/12	Wed 10/31/12	74									
76	Draft 2 Task Force Review	5 d	Thu 11/1/12	Wed 11/7/12	75									
77	Draft 2 Task Force Teleconference Review and Approval	1 d	Thu 11/8/12	Thu 11/8/12	76									
78	Requirements Approved	0 d	Thu 11/8/12	Thu 11/8/12	77									
79	AAMVA ELT Service Requirements Analysis Complete	0 d	Thu 11/8/12	Thu 11/8/12	71				11/8					
80														
81	Pilot State Implementaions	176 d	Thu 1/24/13	Wed 10/2/13										
82	MCO Structured Testing and Support of State Implementations (10 MCO)	176 d	Thu 1/24/13	Wed 10/2/13	51									
83	State Implementations (schedule unknown)	176 d	Thu 1/24/13	Wed 10/2/13	51									
84	State 1 -	8 mo	Thu 1/24/13	Wed 10/2/13										
85	State 2 -	8 mo	Thu 1/24/13	Wed 10/2/13										
86	State 3 -	8 mo	Thu 1/24/13	Wed 10/2/13										
87	State 4 -	8 mo	Thu 1/24/13	Wed 10/2/13										
88	State 5 -	8 mo	Thu 1/24/13	Wed 10/2/13										
89	State 6 -	8 mo	Thu 1/24/13	Wed 10/2/13										
90	State 7 -	8 mo	Thu 1/24/13	Wed 10/2/13										
91	State 8 -	8 mo	Thu 1/24/13	Wed 10/2/13										
92	State 9 -	8 mo	Thu 1/24/13	Wed 10/2/13										
93	State 10 -	8 mo	Thu 1/24/13	Wed 10/2/13										
94														
95	Pilot Operations and Evaluation	154 d	Thu 10/3/13	Thu 5/22/14	19,81									
96	Pilot Operations Technical Support Period	7 mo	Thu 10/3/13	Thu 5/22/14										
97	PMO Support for Collection of Evaluation Data	2 mo	Thu 10/3/13	Fri 12/6/13										
98	PMO Interviews with Pilot Participants and Data Collection	2 mo	Mon 12/9/13	Wed 2/19/14	97									
99	Return on Investment Analysis	44 d	Mon 12/9/13	Wed 2/19/14	97									
100	PMO Support of State ROI Analysis	2 mo	Mon 12/9/13	Wed 2/19/14										
101	State ROI Analysis (schedule unknown)	44 d	Mon 12/9/13	Wed 2/19/14										
102	State 1 -	2 mo	Mon 12/9/13	Wed 2/19/14										
103	State 2 -	2 mo	Mon 12/9/13	Wed 2/19/14										
104	State 3 -	2 mo	Mon 12/9/13	Wed 2/19/14										
105	State 4 -	2 mo	Mon 12/9/13	Wed 2/19/14										
106	State 5 -	2 mo	Mon 12/9/13	Wed 2/19/14										
107	State 6 -	2 mo	Mon 12/9/13	Wed 2/19/14										
108	State 7 -	2 mo	Mon 12/9/13	Wed 2/19/14										
109	State 8 -	2 mo	Mon 12/9/13	Wed 2/19/14										
110	State 9 -	2 mo	Mon 12/9/13	Wed 2/19/14										
111	State 10 -	2 mo	Mon 12/9/13	Wed 2/19/14										
112	Task Force Meeting #2	7 d	Thu 2/20/14	Fri 2/28/14	98,99									
113	Prepare for Meeting #2	5 d	Thu 2/20/14	Wed 2/26/14										
114	Conduct Meeting #2	2 d	Thu 2/27/14	Fri 2/28/14	113									

Project: E-Titling Proof of Concept Date: Wed 4/4/12	Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
	Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Progress	
	Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Jan '12	May '12	Sep '12	Jan '13	May '13	Sep '13	Jan '14	May '14	Sep '14
115	Follow Ups for Meeting #2	5 d	Thu 2/20/14	Wed 2/26/14										
116	Proof of Concept Evaluation Report	48 d	Mon 3/3/14	Wed 5/7/14	112									
117	Draft 1 Development	20 d	Mon 3/3/14	Fri 3/28/14										
118	Draft 1 Review	5 d	Mon 3/31/14	Fri 4/4/14	117									
119	Draft 1 Teleconference	1 d	Mon 4/7/14	Mon 4/7/14	118									
120	Draft 2 Revisions	7 d	Tue 4/8/14	Wed 4/16/14	119									
121	Draft 2 Review	4 d	Thu 4/17/14	Tue 4/22/14	120									
122	Draft 2 Teleconference	1 d	Wed 4/23/14	Wed 4/23/14	121									
123	Draft 3 Revisions	5 d	Thu 4/24/14	Wed 4/30/14	122									
124	Draft 3 Review	4 d	Thu 5/1/14	Tue 5/6/14	123									
125	Draft 3 Teleconference Review and Approval	1 d	Wed 5/7/14	Wed 5/7/14	124									
126	Evaluation Report Approved	0 d	Wed 5/7/14	Wed 5/7/14	125									
127	Best Practices	48 d	Mon 3/3/14	Wed 5/7/14	112									
128	Draft 1 Development	20 d	Mon 3/3/14	Fri 3/28/14										
129	Draft 1 Review	5 d	Mon 3/31/14	Fri 4/4/14	128									
130	Draft 1 Teleconference	1 d	Mon 4/7/14	Mon 4/7/14	129									
131	Draft 2 Revisions	7 d	Tue 4/8/14	Wed 4/16/14	130									
132	Draft 2 Review	4 d	Thu 4/17/14	Tue 4/22/14	131									
133	Draft 2 Teleconference	1 d	Wed 4/23/14	Wed 4/23/14	132									
134	Draft 3 Revisions	5 d	Thu 4/24/14	Wed 4/30/14	133									
135	Draft 3 Review	4 d	Thu 5/1/14	Tue 5/6/14	134									
136	Draft 3 Teleconference Review and Approval	1 d	Wed 5/7/14	Wed 5/7/14	135									
137	Best Practices Approved	0 d	Wed 5/7/14	Wed 5/7/14	136									
138														
139	Closure	11 d	Fri 5/23/14	Mon 6/9/14	95									
140	Transition to Long Term Governance Entity	10 d	Fri 5/23/14	Fri 6/6/14										
141	Package all deliverables for archival	10 d	Fri 5/23/14	Fri 6/6/14										
142	Close out Contracts	10 d	Fri 5/23/14	Fri 6/6/14										
143	Close out Teleconference	1 d	Mon 6/9/14	Mon 6/9/14	140,141,142									
144	Closure Complete	0 d	Mon 6/9/14	Mon 6/9/14	143									
145														
146	Project Stop Date			Mon 6/9/14	139									

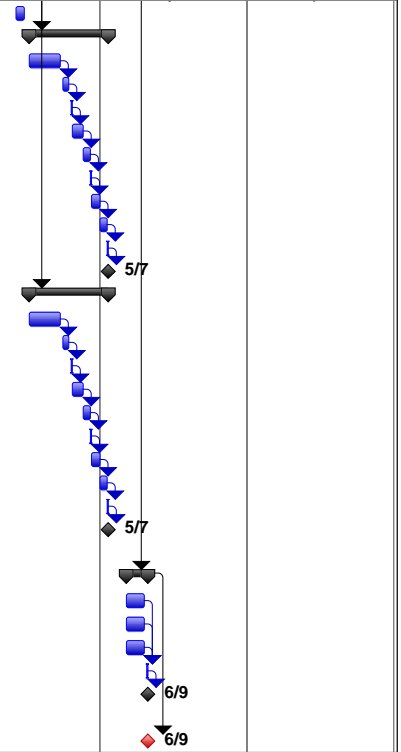

Project: E-Titling Proof of Concept
Date: Wed 4/4/12

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Progress	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Deadline	
